



ID	Task Name	Duration	Start	Finish	01 January		01 May		01 September		01 January		01 May		01 September	
					27/12	21/02	18/04	13/06	08/08	03/10	28/11	23/01	19/03	14/05	09/07	03/09
76	Revision of draft update to PCSR Sub-chapter 10.3 section 7 MSIV	22 days	Mon 06/08/12	Fri 31/08/12												
77	Preparation of draft update to PCSR Sub-chapter 3.1 section 1 MSIV	22 days	Mon 06/08/12	Fri 31/08/12												
78	Preparation of draft update to PCSR Sub-chapter 3.4 section 0 MSIV	22 days	Mon 06/08/12	Fri 31/08/12												
79	Transmission to ONR	0 days	Fri 31/08/12	Fri 31/08/12												
80	ONR Assessment	84 days	Wed 30/05/12	Mon 10/09/12												
81	Update following resolution of ONR comments	10 days	Tue 11/09/12	Fri 21/09/12												
82	Submission of Final PCSR Sub-chapter	0 days	Fri 21/09/12	Fri 21/09/12												
83	Preparation of updates to supporting document PEER-F 102070	59 days	Mon 05/03/12	Tue 15/05/12												
84	Transmission of supporting document - PEER-F 102070	0 days	Tue 15/05/12	Tue 15/05/12												
85	Update of PEER-F 102070 MSIV	22 days	Mon 06/08/12	Fri 31/08/12												
86	Transmission of supporting documents MSIV	0 days	Fri 31/08/12	Fri 31/08/12												
87	Preparation of ENSNDR090183 MSIV	31 days	Mon 11/06/12	Wed 18/07/12												
88	Transmission of supporting documents MSIV	0 days	Wed 18/07/12	Wed 18/07/12												
89	<b>Task 3 Convergence Meetings</b>	<b>82.14 days</b>	<b>Wed 30/05/12</b>	<b>Thu 06/09/12</b>												
90	Convergence Meeting	0 days	Wed 30/05/12	Wed 30/05/12												
91	Final Convergence Meeting	0 days	Thu 06/09/12	Thu 06/09/12												
92																
93	<b>Issue SI01 Action 4 Non Destructive testing of RCP Repair welds</b>	<b>365.57 days</b>	<b>Mon 13/06/11</b>	<b>Fri 31/08/12</b>												
94	<b>Task 1 Production of reports &amp; ONR Assessment</b>	<b>273.57 days</b>	<b>Mon 13/06/11</b>	<b>Fri 11/05/12</b>												
95	Preparation of RCP NDT Test report EFFQM 10.17210	24 days	Mon 13/06/11	Tue 12/07/11												
96	Submission of report to ONR	0 days	Tue 12/07/11	Tue 12/07/11												
97	Update of RCP NDT Report PEEM-F 10.2218	38 days	Mon 01/08/11	Thu 15/09/11												
98	Submission of report to ONR	0 days	Thu 15/09/11	Thu 15/09/11												
99	ONR assessment of deliverables	211 days	Mon 18/07/11	Fri 30/03/12												
100	RP response to ONR queries	245 days	Mon 18/07/11	Fri 11/05/12												
101	Update of RCP NDT Test report EFFQM 10.17210 for TQ1464	68 days	Mon 25/07/11	Fri 14/10/11												
102	Submission of report to ONR	0 days	Fri 14/10/11	Fri 14/10/11												
103	<b>Task 2 Update of PCSR &amp; Supporting Documents</b>	<b>148.43 days</b>	<b>Mon 05/03/12</b>	<b>Fri 31/08/12</b>												
104	Preparation of draft update to PCSR Sub-chapter 5.4 section 1	59 days	Mon 05/03/12	Tue 15/05/12												
105	Transmission to ONR	0 days	Tue 15/05/12	Tue 15/05/12												
106	ONR Assessment	41 days	Fri 18/05/12	Fri 06/07/12												
107	Update following resolution of ONR comments	28 days	Mon 30/07/12	Fri 31/08/12												
108	Submission of updated PCSR Sub-chapter	0 days	Fri 31/08/12	Fri 31/08/12												
109	Preparation of updates to supporting document PEER-F 102070	59 days	Mon 05/03/12	Tue 15/05/12												
110	Transmission of supporting document - PEER-F 102070	0 days	Tue 15/05/12	Tue 15/05/12												
111	<b>Task 3 Convergence Meetings</b>	<b>0 days</b>	<b>Wed 30/05/12</b>	<b>Wed 30/05/12</b>												
112	Convergence Meeting	0 days	Wed 30/05/12	Wed 30/05/12												
113																
114	<b>Issue SI01 Action 5 FMA &amp; NDT of RCP flywheel</b>	<b>359.71 days</b>	<b>Mon 20/06/11</b>	<b>Fri 31/08/12</b>												
115	<b>Task 1 Production of reports &amp; ONR Assessment</b>	<b>268.29 days</b>	<b>Mon 20/06/11</b>	<b>Fri 11/05/12</b>												
116	Update of RCP flywheel FMA report PEER-F 10.1674	58 days	Mon 20/06/11	Mon 29/08/11												
117	Submission of report to ONR	0 days	Tue 30/08/11	Tue 30/08/11												
118	Update of RCP flywheel NDT report PEEO-F 10.0715	32 days	Thu 21/07/11	Mon 29/08/11												
119	Submission of report to ONR	0 days	Tue 30/08/11	Tue 30/08/11												
120	Preparation of RCP flywheel ISI principles report ECEMA111847	52 days	Mon 27/06/11	Mon 29/08/11												
121	Submission of report to ONR	0 days	Tue 30/08/11	Tue 30/08/11												
122	ONR assessment of deliverables	190 days	Thu 11/08/11	Fri 30/03/12												
123	RP response to ONR queries	225 days	Thu 11/08/11	Fri 11/05/12												
124	Update of RCP flywheel FMA report PEER-F 10.1674 for TQ1477	81 days	Fri 02/09/11	Fri 09/12/11												
125	Submission of report to ONR	0 days	Fri 09/12/11	Fri 09/12/11												
126	Update of RCP flywheel NDT report PEEO-F 10.0715 for TQ1477	81 days	Fri 02/09/11	Fri 09/12/11												
127	Submission of report to ONR	0 days	Fri 09/12/11	Fri 09/12/11												
128	<b>Task 2 Update of PCSR &amp; Supporting Documents</b>	<b>148.43 days</b>	<b>Mon 05/03/12</b>	<b>Fri 31/08/12</b>												
129	Preparation of draft update to PCSR Sub-chapter 5.4 section 1	59 days	Mon 05/03/12	Tue 15/05/12												
130	Transmission to ONR	0 days	Tue 15/05/12	Tue 15/05/12												
131	ONR Assessment	44 days	Tue 15/05/12	Fri 06/07/12												
132	Update following resolution of ONR comments	22 days	Mon 06/08/12	Fri 31/08/12												
133	Submission of updated PCSR Sub-chapter	0 days	Fri 31/08/12	Fri 31/08/12												
134	Preparation of updates to supporting document PEER-F 102070, if required	59 days	Mon 05/03/12	Tue 15/05/12												
135	Transmission of supporting document - PEER-F 102070, if required	0 days	Tue 15/05/12	Tue 15/05/12												
136	<b>Task 3 Convergence Meetings</b>	<b>0 days</b>	<b>Wed 30/05/12</b>	<b>Wed 30/05/12</b>												
137	Convergence Meeting	0 days	Wed 30/05/12	Wed 30/05/12												
138																
139	<b>Issue SI01 Action 6 Prototype Application NDT technical Justification</b>	<b>245.71 days</b>	<b>Wed 03/08/11</b>	<b>Wed 30/05/12</b>												
140	<b>Task 1 Production of reports &amp; ONR Assessment</b>	<b>231.14 days</b>	<b>Wed 03/08/11</b>	<b>Fri 11/05/12</b>												
141	Update of NDT Technical Justification report PEEM-F 10.2217	56 days	Wed 03/08/11	Tue 11/10/11												
142	Submission of report to ONR	0 days	Wed 12/10/11	Wed 12/10/11												
143	ONR assessment of deliverables	148 days	Mon 03/10/11	Fri 30/03/12												
144	RP response to ONR queries	182 days	Mon 03/10/11	Fri 11/05/12												
145	<b>Task 2 Update of PCSR &amp; Supporting Documents</b>	<b>59 days</b>	<b>Mon 05/03/12</b>	<b>Tue 15/05/12</b>												
146	Preparation of updates to supporting document PEER-F 102070	59 days	Mon 05/03/12	Tue 15/05/12												
147	Transmission of supporting document - PEER-F 102070	0 days	Tue 15/05/12	Tue 15/05/12												
148	<b>Task 3 Convergence Meetings</b>	<b>0 days</b>	<b>Wed 30/05/12</b>	<b>Wed 30/05/12</b>												
149	Task 3 Convergence Meeting	0 days	Wed 30/05/12	Wed 30/05/12												
150																



ID	Task Name	Duration	Start	Finish	01 January		01 May	01 September			01 January		01 May		01 September					
					27/12	21/02	18/04	13/06	08/08	03/10	28/11	23/01	19/03	14/05	09/07	03/09	29/10			
151	<b>Issue SI01 Action 7 Non Destructive testing of MCL &amp; DMW</b>	<b>369 days</b>	<b>Wed 08/06/11</b>	<b>Fri 31/08/12</b>																
152	<b>Task 1 Production of reports &amp; ONR Assessment</b>	<b>279 days</b>	<b>Wed 08/06/11</b>	<b>Tue 15/05/12</b>																
153	Preparation of MCL weld connection design basis report PEER-F DC 60A	65 days	Mon 20/06/11	Tue 06/09/11																
154	Submission of report to ONR	0 days	Wed 07/09/11	Wed 07/09/11																
155	Update MCL UT capability report PEEM-F 11.0505A	54 days	Fri 01/07/11	Tue 06/09/11																
156	Submission of report to ONR	0 days	Wed 07/09/11	Wed 07/09/11																
157	ONR Letter EPR70373R	0 days	Fri 14/10/11	Fri 14/10/11																
158	PEER-F DC 78 ALARP Justification	80 days	Mon 07/11/11	Fri 10/02/12																
159	Submission of report to ONR	0 days	Fri 10/02/12	Fri 10/02/12																
160	PEER-F DC 73 MCL Optimisation - U Leg Lowering Feasibility Studies	131 days	Mon 05/09/11	Fri 10/02/12																
161	Submission of report to ONR	0 days	Fri 10/02/12	Fri 10/02/12																
162	PEPR-F 11.1421 Intermediate Large Break LOCA Feasibility Study	131 days	Mon 05/09/11	Fri 10/02/12																
163	Submission of report to ONR	0 days	Fri 10/02/12	Fri 10/02/12																
164	Update MCL UT capability report PEEM-F 11.0505B	98 days	Fri 14/10/11	Fri 10/02/12																
165	Submission of report to ONR	0 days	Fri 10/02/12	Fri 10/02/12																
166	EFFQM/12.17004 B Test Report Ultrasonic Examination of SG safe-end NGT proces	91 days	Mon 24/10/11	Fri 10/02/12																
167	Submission of report to ONR	0 days	Fri 10/02/12	Fri 10/02/12																
168	TD/RB/REP069 Issue 1 - Capability of Ultrasonic Inspection Procedures	79 days	Mon 07/11/11	Fri 10/02/12																
169	Submission of report to ONR	0 days	Fri 10/02/12	Fri 10/02/12																
170	PEER-F DC 79 A MCL Optimisation - Counterbore Length Increase Feasibility Study	87 days	Thu 27/10/11	Fri 10/02/12																
171	Submission of report to ONR	0 days	Fri 10/02/12	Fri 10/02/12																
172	Preparation of MSL UT capability report PEEM-F 11.0959	42 days	Wed 08/06/11	Thu 28/07/11																
173	Submission of report to ONR	0 days	Fri 29/07/11	Fri 29/07/11																
174	ONR assessment of deliverables	211 days	Mon 18/07/11	Fri 30/03/12																
175	RP response to ONR queries	247 days	Mon 18/07/11	Tue 15/05/12																
176	Update of MSL UT capability report PEEM-F 11.0959 for TQ1516	122 days	Thu 10/11/11	Fri 06/04/12																
177	Submission of report to ONR	0 days	Fri 06/04/12	Fri 06/04/12																
178	<b>Task 2 Update of PCSR &amp; Supporting Documents</b>	<b>148.43 days</b>	<b>Mon 05/03/12</b>	<b>Fri 31/08/12</b>																
179	Preparation of draft update to PCSR Sub-chapter 5.2 section 5	59 days	Mon 05/03/12	Tue 15/05/12																
180	Preparation of draft update to PCSR Sub-chapter 5.3 section 7	59 days	Mon 05/03/12	Tue 15/05/12																
181	Preparation of draft update to PCSR Sub-chapter 5.4 section 2	59 days	Mon 05/03/12	Tue 15/05/12																
182	Preparation of draft update to PCSR Sub-chapter 5.4 section 3	59 days	Mon 05/03/12	Tue 15/05/12																
183	Preparation of draft update to PCSR Sub-chapter 17.5 section 3	59 days	Mon 05/03/12	Tue 15/05/12																
184	Preparation of draft update to PCSR Sub-chapter 10.3 section 6	59 days	Mon 05/03/12	Tue 15/05/12																
185	Transmission to ONR	0 days	Tue 15/05/12	Tue 15/05/12																
186	ONR Assessment	42 days	Thu 17/05/12	Fri 06/07/12																
187	Update following resolution of ONR comments	22 days	Mon 06/08/12	Fri 31/08/12																
188	Submission of updated PCSR Sub-chapter	0 days	Fri 31/08/12	Fri 31/08/12																
189	Preparation of updates to supporting document PEER-F 102070	59 days	Mon 05/03/12	Tue 15/05/12																
190	Transmission of supporting document - PEER-F 102070	0 days	Tue 15/05/12	Tue 15/05/12																
191	<b>Task 3 Convergence Meetings</b>	<b>190.86 days</b>	<b>Mon 10/10/11</b>	<b>Wed 30/05/12</b>																
192	Technical Review Meeting	0 days	Mon 10/10/11	Mon 10/10/11																
193	Technical Review Meeting	0 days	Tue 10/01/12	Tue 10/01/12																
194	Convergence Meeting	0 days	Wed 30/05/12	Wed 30/05/12																

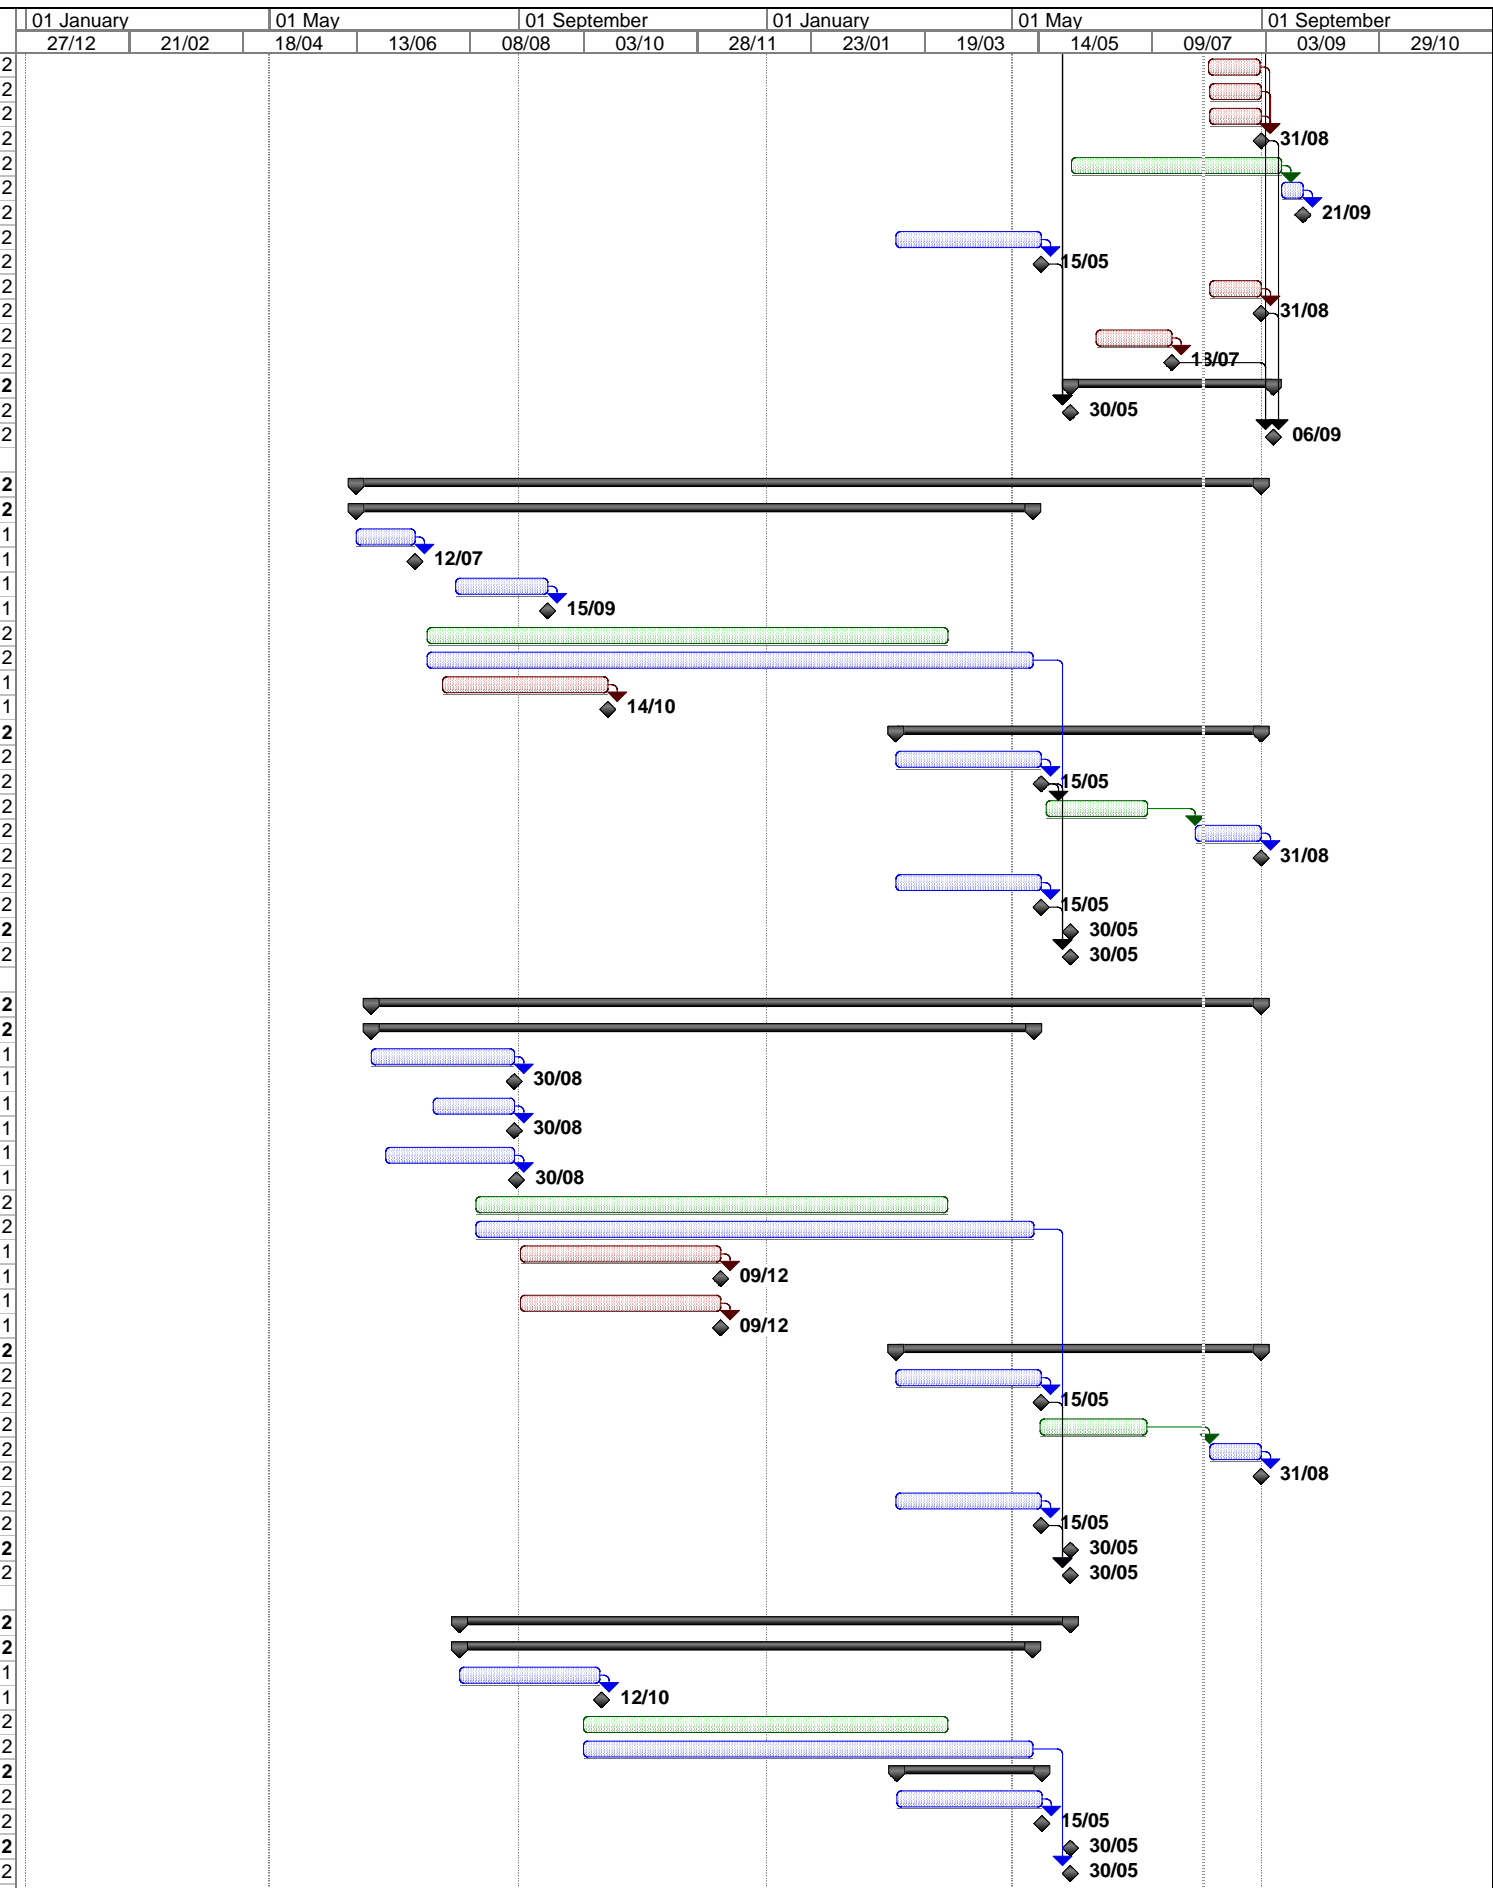
