ID		Task Name	Duration	Start	Finish
1		**Issue SI02 Action 1 Principles of RPV Surveillance scheme**	**348.14 days**	**Mon 04/04/11**	**Fri 01/06/12**
2		**Task 1 Production of Reports & ONR Assessment**	**324.71 days**	**Mon 04/04/11**	**Fri 04/05/12**
3	✓	Letter ND(NII) EPR00640R	0 days	Mon 04/04/11	Mon 04/04/11
4	✓	Action 1.1 Deliverables: Implications of Neutron Energy Spectra - RP Position Report & 2 s	0 days	Fri 06/05/11	Fri 06/05/11
5		Action 1.2 Deliverables: Justification of the concepts - ESTEREL Programme Report	41 days	Fri 10/06/11	Fri 29/07/11
6		Transmission to ONR	0 days	Fri 29/07/11	Fri 29/07/11
7		ONR Letter EPR70382R on RPV ISP	0 days	Thu 17/11/11	Thu 17/11/11
8		RPV ISP design Principles for UK EPR Report H-T27-2012-00181-EN	86 days	Mon 07/11/11	Mon 20/02/12
9		Transmission to ONR	0 days	Mon 20/02/12	Mon 20/02/12
10		ONR Assessment of Action deliverables	211 days	Mon 18/07/11	Fri 30/03/12
11		RP responses to ONR Queries	239 days	Mon 18/07/11	Fri 04/05/12
12		**Task 2 Update of PCSR & Supporting Documents**	**84.57 days**	**Mon 20/02/12**	**Fri 01/06/12**
13		Prepare draft PCSR update section 5.3.7	62 days	Mon 20/02/12	Fri 04/05/12
14		Transmission to ONR	0 days	Fri 04/05/12	Fri 04/05/12
15		ONR Assessment of draft PCSR update 5.3.7	12 days	Fri 04/05/12	Fri 18/05/12
16		Prepare final PCSR update integrating ONR comments	11 days	Mon 21/05/12	Fri 01/06/12
17		Transmission to ONR	0 days	Fri 01/06/12	Fri 01/06/12
18		**Task 3 Convergence meetings**	**187.43 days**	**Thu 13/10/11**	**Wed 30/05/12**
19		Technical Review Meeting	0 days	Thu 13/10/11	Thu 13/10/11
20		Technical Review Meeting	0 days	Fri 06/01/12	Fri 06/01/12
21		Convergence meeting	0 days	Wed 30/05/12	Wed 30/05/12

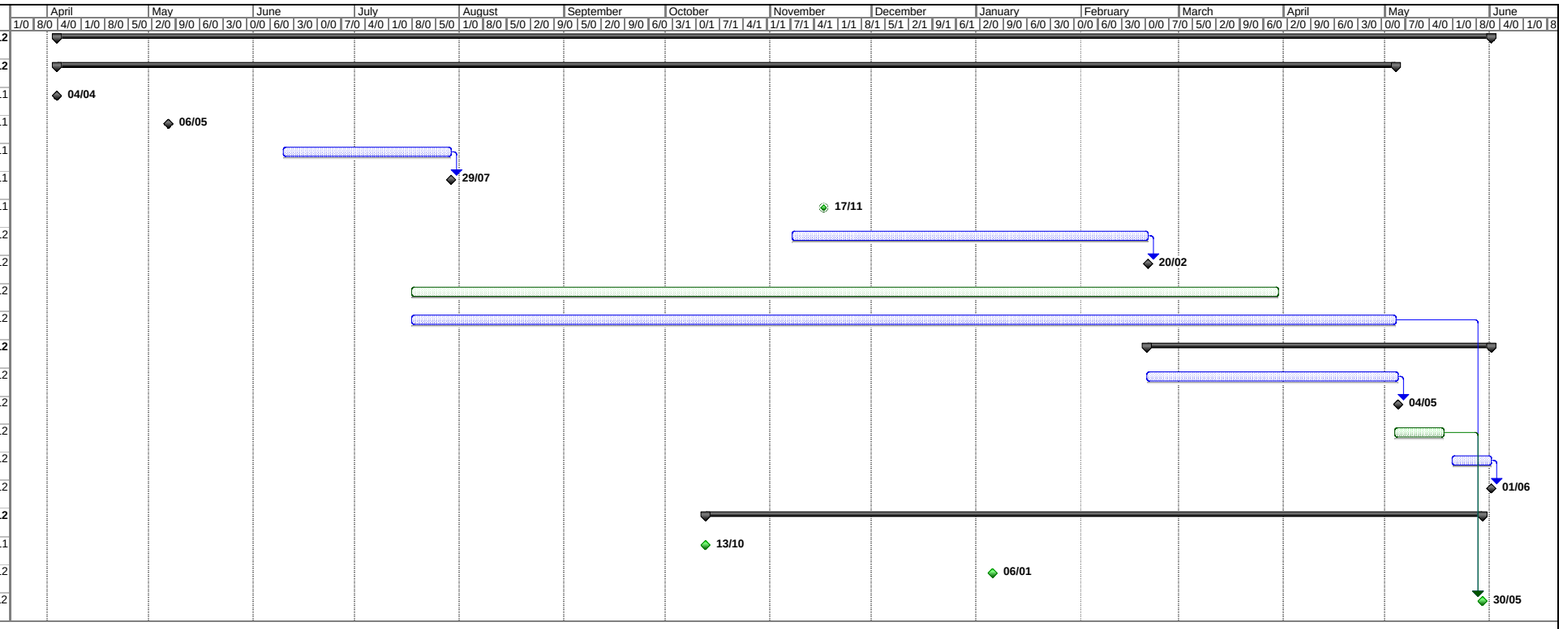

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
